

Project : 13C068(0)


READSBORO BF 0102(16)

								22	24	
Activity Name	Activity Description	Rem. Dur.	Orig. Dur.	early start date	early finish date	VTRANS OBS	VTRANS WBS			
010.005	Scoping Funded	0	22	31Jan13	04Mar13	PROJECT DEVELOPMENT	010			
010.01	PE/Pre-Appraisal Authorized	0	22	07Oct14	15Oct14	POLICY & PLANNING	010			
020.06	Local Concerns Letter	0	33	23May13	02Jul13	PROJECT DEVELOPMENT	020			
030.01.01	Survey	0	33	29Mar13	14May13	SURVEY	030.01			
030.01.02	Traffic Data	0	22	08Apr13	28May13	TECHNICAL SUPPORT	030.01			
030.01.03	Hydraulics - Preliminary	0	22	20May13	13Jun13	HYDRAULICS	030.01			
030.01.04	Utilities - Existing	0	22	20May13	13Jun13	UTILITIES	030.01			
030.01.05	ROW - Existing	0	22	20May13	17Jun13	RIGHT-OF-WAY	030.01			
030.01.06	Archaeological Resource Identification	0	22	10Apr13	30May13	ENVIRONMENTAL	030.01			
030.01.07	Historical Resource Identification	0	22	10Apr13	14May13	ENVIRONMENTAL	030.01			
030.01.08	Biological Resource Identification	0	22	10Apr13	21May13	ENVIRONMENTAL	030.01			
030.01.90	Resource Plotting	0	22	10Apr13	10Jun13	ENVIRONMENTAL	030.01			
030.04.01	Develop Alternatives	0	22	02Jul13	10Oct13	PROJECT DEVELOPMENT	030.04			
030.04.015	Management Approval Of Scope	0	11	10Oct13	17Oct13	PROJECT DEVELOPMENT	030.04			
030.04.02	Alternatives Presentation/Refinement	0	44	17Oct13	10Dec13	PROJECT DEVELOPMENT	030.04			
030.04.03	Alternative Accepted	0	0	07Oct14	07Oct14	PROJECT DEVELOPMENT	030.04			
030.04.05	Geotechnical Assessment	0	22	20May13	26Jul13	MATERIALS & RESEARCH	030.04			
040.04	NEPA Document	0	132	08Feb17	11Jan18	ENVIRONMENTAL	040			
050.01	Develop Conceptual Plans	0	22	14Feb15	30Mar15	PROJECT DEVELOPMENT	050			
050.02	Public Meeting/Hearing/Refinement	0	32	02Feb18	21Mar18	PROJECT DEVELOPMENT	050			
050.03	Project Defined	0	0	22Mar18	22Mar18	PROJECT DEVELOPMENT	050			
060.01	Develop Preliminary Plans	0	132	18Sep15	05Oct17	PROJECT DEVELOPMENT	060			
060.011	Preliminary Risk Registry	0	30	01Sep17	05Oct17	PROJECT DEVELOPMENT	060			
060.012	Preliminary Transportation Management Plan	0	30	01Sep17	05Oct17	PROJECT DEVELOPMENT	060			
060.0125	Preliminary Plans Internal Review	0	22	05Oct17	20Oct17	PROJECT DEVELOPMENT	060			
060.013	Preliminary Plans QAU Review Period	0	29	11Dec17	08Jan18	PROJECT DEVELOPMENT	060			
060.014	Preliminary Plans Constructability Review - Meeting	0	10	13Jan18	31Jan18	PROJECT DEVELOPMENT	060			
060.03	Geotechnical Analysis	0	110	14Nov15	15Jan17	MATERIALS & RESEARCH	060			
060.04	Hydraulics - Final	0	33	02Oct17	08Dec17	HYDRAULICS	060			
060.05	Environmental Permits	3	120	07Jun23	05Feb24	ENVIRONMENTAL	060			

Project : 13C068(0)

READSBORO BF 0102(16)

							22	24	
Activity Name	Activity Description	Rem. Dur.	Orig. Dur.	early start date	early finish date	VTRANS OBS	VTRANS WBS		
060.06	Utility Relocation Routing	0	55	26Mar16	02Jun17	UTILITIES	060		
060.07	Property Owner Contact	0	44	02Feb18	22Mar18	PROJECT DEVELOPMENT	060		
060.08	Address Prelim plans comments	0	30	02Feb18	13Apr18	PROJECT DEVELOPMENT	060		
060.085	Preliminary ROW Estimate/ROW STIP Verification	0	30	13Apr18	22May18	PROJECT DEVELOPMENT	060		
060.09	ROW Acquisition Authorization	0	15	30Apr18	21May18	RIGHT-OF-WAY	060		
060.10	NEPA Re-Eval	0	44	07Jun23	05Oct23	UTILITIES	060		
060.11	Utility Agreements	0	88	02Apr16	29Mar17	UTILITIES	060		
080.01	Develop ROW Plans and Titles	0	88	29May18	14Mar19	RIGHT-OF-WAY	080		
080.02	Legal Document Preparation	0	33	14Mar19	16May19	RIGHT-OF-WAY	080		
080.03	Final ROW Plans and Documents Complete	0	0	16May19	16May19	RIGHT-OF-WAY	080		
090.02	Appraisal	0	75	22May18	15Aug18	RIGHT-OF-WAY	090		
090.022	Waiver Valuation Estimates	0	22	23Jul19	06Sep19	RIGHT-OF-WAY	090		
090.024	Appraisal Review	0	22	18Aug18	19Sep18	RIGHT-OF-WAY	090		
090.03	Negotiation	84	100	11Jul19	31May24	RIGHT-OF-WAY	090		
090.037	Minor Alterations Condemnation	66	66	22Mar24	24Jun24	RIGHT-OF-WAY	090		
090.04	Compensation	15	15	25Jun24	16Jul24	RIGHT-OF-WAY	090		
090.05	ROW Clear	0	0	15Jul24	15Jul24	RIGHT-OF-WAY	090		
100.01	Develop Final Plans, Specifications & Estimate	11	120	05Mar23	15Feb24	PROJECT DEVELOPMENT	100		
100.011	Final Risk Registry	0	120	15Oct20	05Dec20	PROJECT DEVELOPMENT	100		
100.012	Final Transportation Management Plan	0	33	15Oct20	05Dec20	PROJECT DEVELOPMENT	100		
100.02	Final Plans, Specifications & Estimate/QA Review Period	22	22	04Mar24	03Apr24	PROJECT DEVELOPMENT	100		
100.025	Final Plans, Specifications & Estimate Review Meeting	10	10	28Mar24	10Apr24	PROJECT DEVELOPMENT	100		
100.03	Utility Clearance & Special Provisions	10	10	16Jul24	29Jul24	UTILITIES	100		
100.10	Develop Contract Plans	0	44	31Aug21	12Nov21	PROJECT DEVELOPMENT	100		
100.106	Contract Plan Re-Evaluation	44	44	14May24	16Jul24				
100.11	Submit Contract Plans	0	0	03Feb22	03Feb22	PROJECT DEVELOPMENT	100		
100.11.50	Resubmit Contract Plans for re-advertisement	0	0	16Jul24	16Jul24	PROJECT DEVELOPMENT	100		
110.01	Proposal Preparation	20	20	17Jul24	13Aug24	FINANCE & ADMINISTRATION	110		
110.02	Advertisement	0	23	02Mar22	15Apr22	FINANCE & ADMINISTRATION	110		
110.02.50	Re-Advertisement	21	21	14Aug24	13Sep24	FINANCE & ADMINISTRATION	110		

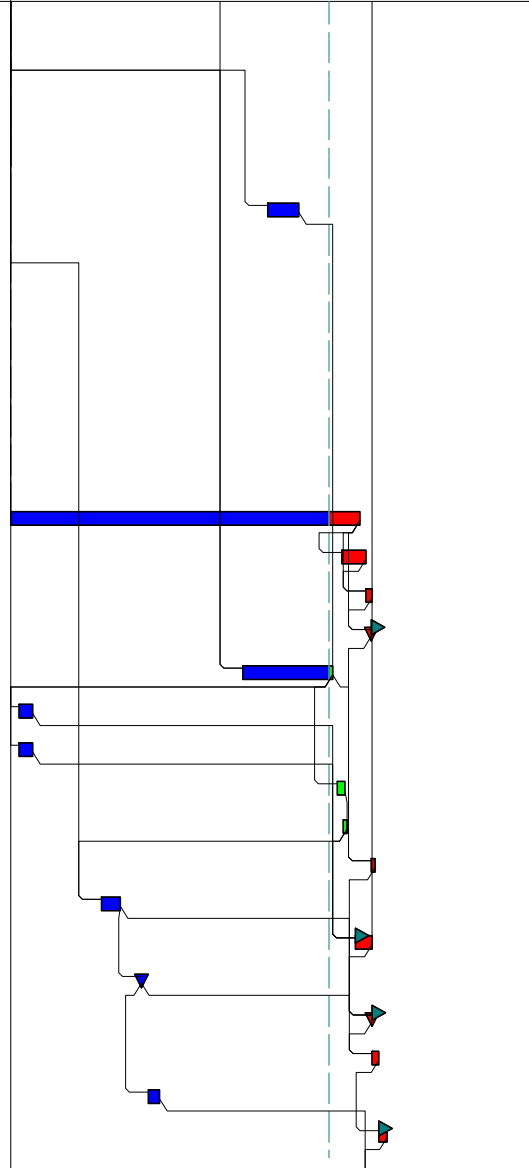

Project : 13C068(0)

READSBORO BF 0102(16)

Activity Name	Activity Description	Rem. Dur.	Orig. Dur.	early start date	early finish date	VTRANS OBS	VTRANS WBS	22	24
110.03	Contract Award	22	22	16Sep24	15Oct24	FINANCE & ADMINISTRATION	110		
120.10	Pre-Construction	122	122	16Oct24	15Apr25	PROJECT DEVELOPMENT	120		
120.11	Active Construction	665	665	16Apr25	12Nov27	PROJECT DEVELOPMENT	120		

